Baseline Schedule - DRAFT
Maillet, Sommes and Morgan Constructed Wetlands
Reading, MA
T Ford Company, Inc.

ID	Task Name	Duration	Start	Finish	Predecessors
1					
2	Survey Layout, Test Pits, & Pre-Mob.	26 days	Fri 6/23/23	Fri 7/28/23	
3	Mobilization & Trail Closure	1 day	Mon 7/31/23	Mon 7/31/23	2
4	**Remove Invasives**	**166 days**	**Tue 8/1/23**	**Tue 3/19/24**	
5	Treatment 1 - Mowing / Clearing	1 day	Tue 8/1/23	Tue 8/1/23	3
6	Treatment 2 - Mowing / Earth	1 day	Mon 9/11/23	Mon 9/11/23	20,5
7	Treatment 3 - Prior to Fine Grading East - TBD	2 days	Mon 11/6/23	Tue 11/7/23	6,31
8	Treatment 4 - Prior to Fine Grading West -	2 days	Mon 3/18/24	Tue 3/19/24	7,53
9	**Remove Trees**	**17 days**	**Mon 7/31/23**	**Tue 8/22/23**	
10	Tree Clearing Along MBTA ROW	2 days	Mon 7/31/23	Tue 8/1/23	
11	Tree Clearing of Remaining Site	5 days	Mon 7/31/23	Fri 8/4/23	
12	Grubbing	2 days	Mon 8/21/23	Tue 8/22/23	13
13	**Erosion Controls**	**10 days**	**Mon 8/7/23**	**Fri 8/18/23**	
14	Temporary Fence	1 day	Mon 8/7/23	Mon 8/7/23	10,11
15	Snow Fence, Silt Sock & Tree	10 days	Mon 8/7/23	Fri 8/18/23	10,11
16	Construction Entra	2 days	Tue 8/8/23	Wed 8/9/23	10,14
17	**Stump Removal**	**10 days**	**Mon 8/21/23**	**Fri 9/1/23**	**13**
18	Excavate Stumps & Fill Depressions	5 days	Mon 8/21/23	Fri 8/25/23	13
19	Load out Stumps	5 days	Mon 8/28/23	Fri 9/1/23	18
20	Strip & Stockpile Loar	5 days	Mon 9/4/23	Fri 9/8/23	19
21	Fire Hydrant Installati	5 days	Mon 9/11/23	Fri 9/15/23	20
22	**East End - Grading, Drainage, Masonry & Landscape**	**70 days**	**Mon 9/11/23**	**Fri 12/15/23**	
23	**Rough Grading**	**10 days**	**Mon 9/18/23**	**Fri 9/29/23**	
24	Forebays	5 days	Mon 9/18/23	Fri 9/22/23	20,21
25	Constructed Wetland: Cell 1	5 days	Mon 9/25/23	Fri 9/29/23	24
26	**Drainage**	**30 days**	**Mon 9/11/23**	**Fri 10/20/23**	
27	Lowell Street Drainage Tie-In	5 days	Mon 9/11/23	Fri 9/15/23	19,20
28	Remainder of Closed Drainage (DMH 120 to	5 days	Mon 9/25/23	Fri 9/29/23	27,24
29	Stone Outlet / Stone Spillways / Concrete	15 days	Mon 10/2/23	Fri 10/20/23	23
30	Masonry - Stone W	10 days	Mon 10/2/23	Fri 10/13/23	23
31	Fine Grading	10 days	Mon 10/23/23	Fri 11/3/23	23,26
32	Re-Spread Loam	10 days	Mon 11/6/23	Fri 11/17/23	31
33	**Landscape**	**25 days**	**Mon 11/13/23**	**Fri 12/15/23**	
34	Seeding	5 days	Mon 11/20/23	Fri 11/24/23	32
35	Planting	10 days	Mon 11/20/23	Fri 12/1/23	32
36	Trees and Shrub	10 days	Mon 12/4/23	Fri 12/15/23	34,35,32
37	Mulch Path	5 days	Mon 11/13/23	Fri 11/17/23	32
38	**Excess Soils**	**50 days**	**Mon 10/2/23**	**Fri 12/8/23**	
39	Load Out Excess East End Soils	5 days	Mon 10/2/23	Fri 10/6/23	23
40	Load Out Excess West End Soils	5 days	Mon 12/4/23	Fri 12/8/23	43
41	Excavation of Hot Spot Soils West	10 days	Mon 10/9/23	Fri 10/20/23	39
42	Load Out of Hot Spot Soils	5 days	Mon 10/23/23	Fri 10/27/23	41
43	**West - End Rough Grading**	**25 days**	**Mon 10/30/23**	**Fri 12/1/23**	
44	Forebay	5 days	Mon 10/30/23	Fri 11/3/23	42
45	Constructed Wetland: Cell 2 & 3 / Connection	20 days	Mon 11/6/23	Fri 12/1/23	42,44
46	Retaining Wall #1 - Entrance Block Walls	15 days	Mon 11/20/23	Fri 12/8/23	20,21,42
47	**West - End Drainage**	**65 days**	**Mon 12/4/23**	**Fri 3/1/24**	
48	Reverse Slope Pipe	5 days	Mon 12/4/23	Fri 12/8/23	45
49	Stone Outlet / Stone Spillways E / Concrete Pavers	15 days	Mon 12/11/23	Fri 12/29/23	43,48
50	Winter Slow Down	45 days	Mon 1/1/24	Fri 3/1/24	
51	**West - End Masonry, Fine Grading & Landscape**	**35 days**	**Mon 3/4/24**	**Fri 4/19/24**	**50**
52	Masonry - Piers	10 days	Mon 3/4/24	Fri 3/15/24	
53	Fine Grading	10 days	Mon 3/4/24	Fri 3/15/24	47
54	Re-Spread Loam	5 days	Mon 3/18/24	Fri 3/22/24	53
55	**Landscape**	**35 days**	**Mon 3/4/24**	**Fri 4/19/24**	**50**
56	Seeding	5 days	Mon 3/25/24	Fri 3/29/24	54
57	Planting	10 days	Mon 3/25/24	Fri 4/5/24	54
58	Trees and Shrub	10 days	Mon 4/8/24	Fri 4/19/24	54,56,57
59	Mulch Path	5 days	Mon 3/4/24	Fri 3/8/24	54
60	Retaining Wall #2 - Parking Lot Block	10 days	Mon 3/4/24	Fri 3/15/24	46,50
61	**Stone Dust Paths**	**20 days**	**Mon 4/1/24**	**Fri 4/26/24**	
62	East - End	10 days	Mon 4/1/24	Fri 4/12/24	
63	West - End	10 days	Mon 4/15/24	Fri 4/26/24	62
64	**Boardwalks**	**30 days**	**Mon 4/29/24**	**Fri 6/7/24**	**61**
65	Boardwalk A & B	10 days	Mon 4/29/24	Fri 5/10/24	62
66	Boardwalk C, D, &	10 days	Mon 5/27/24	Fri 6/7/24	63,67
67	Boardwalk Crossing 10' W x	10 days	Mon 5/13/24	Fri 5/24/24	65
68	**Site Finishes**	**10 days**	**Mon 4/22/24**	**Fri 5/3/24**	**51**
69	152' L Metal & 276' L Rustic	10 days	Mon 4/22/24	Fri 5/3/24	
70	Benches	2 days	Mon 4/22/24	Tue 4/23/24	
71	Sign Installations	3 days	Mon 4/22/24	Wed 4/24/24	
72	Paving & Striping	4 days	Mon 5/6/24	Thu 5/9/24	68
73	Demobilization and Punchlist	15 days	Mon 6/10/24	Fri 6/28/24	72,64

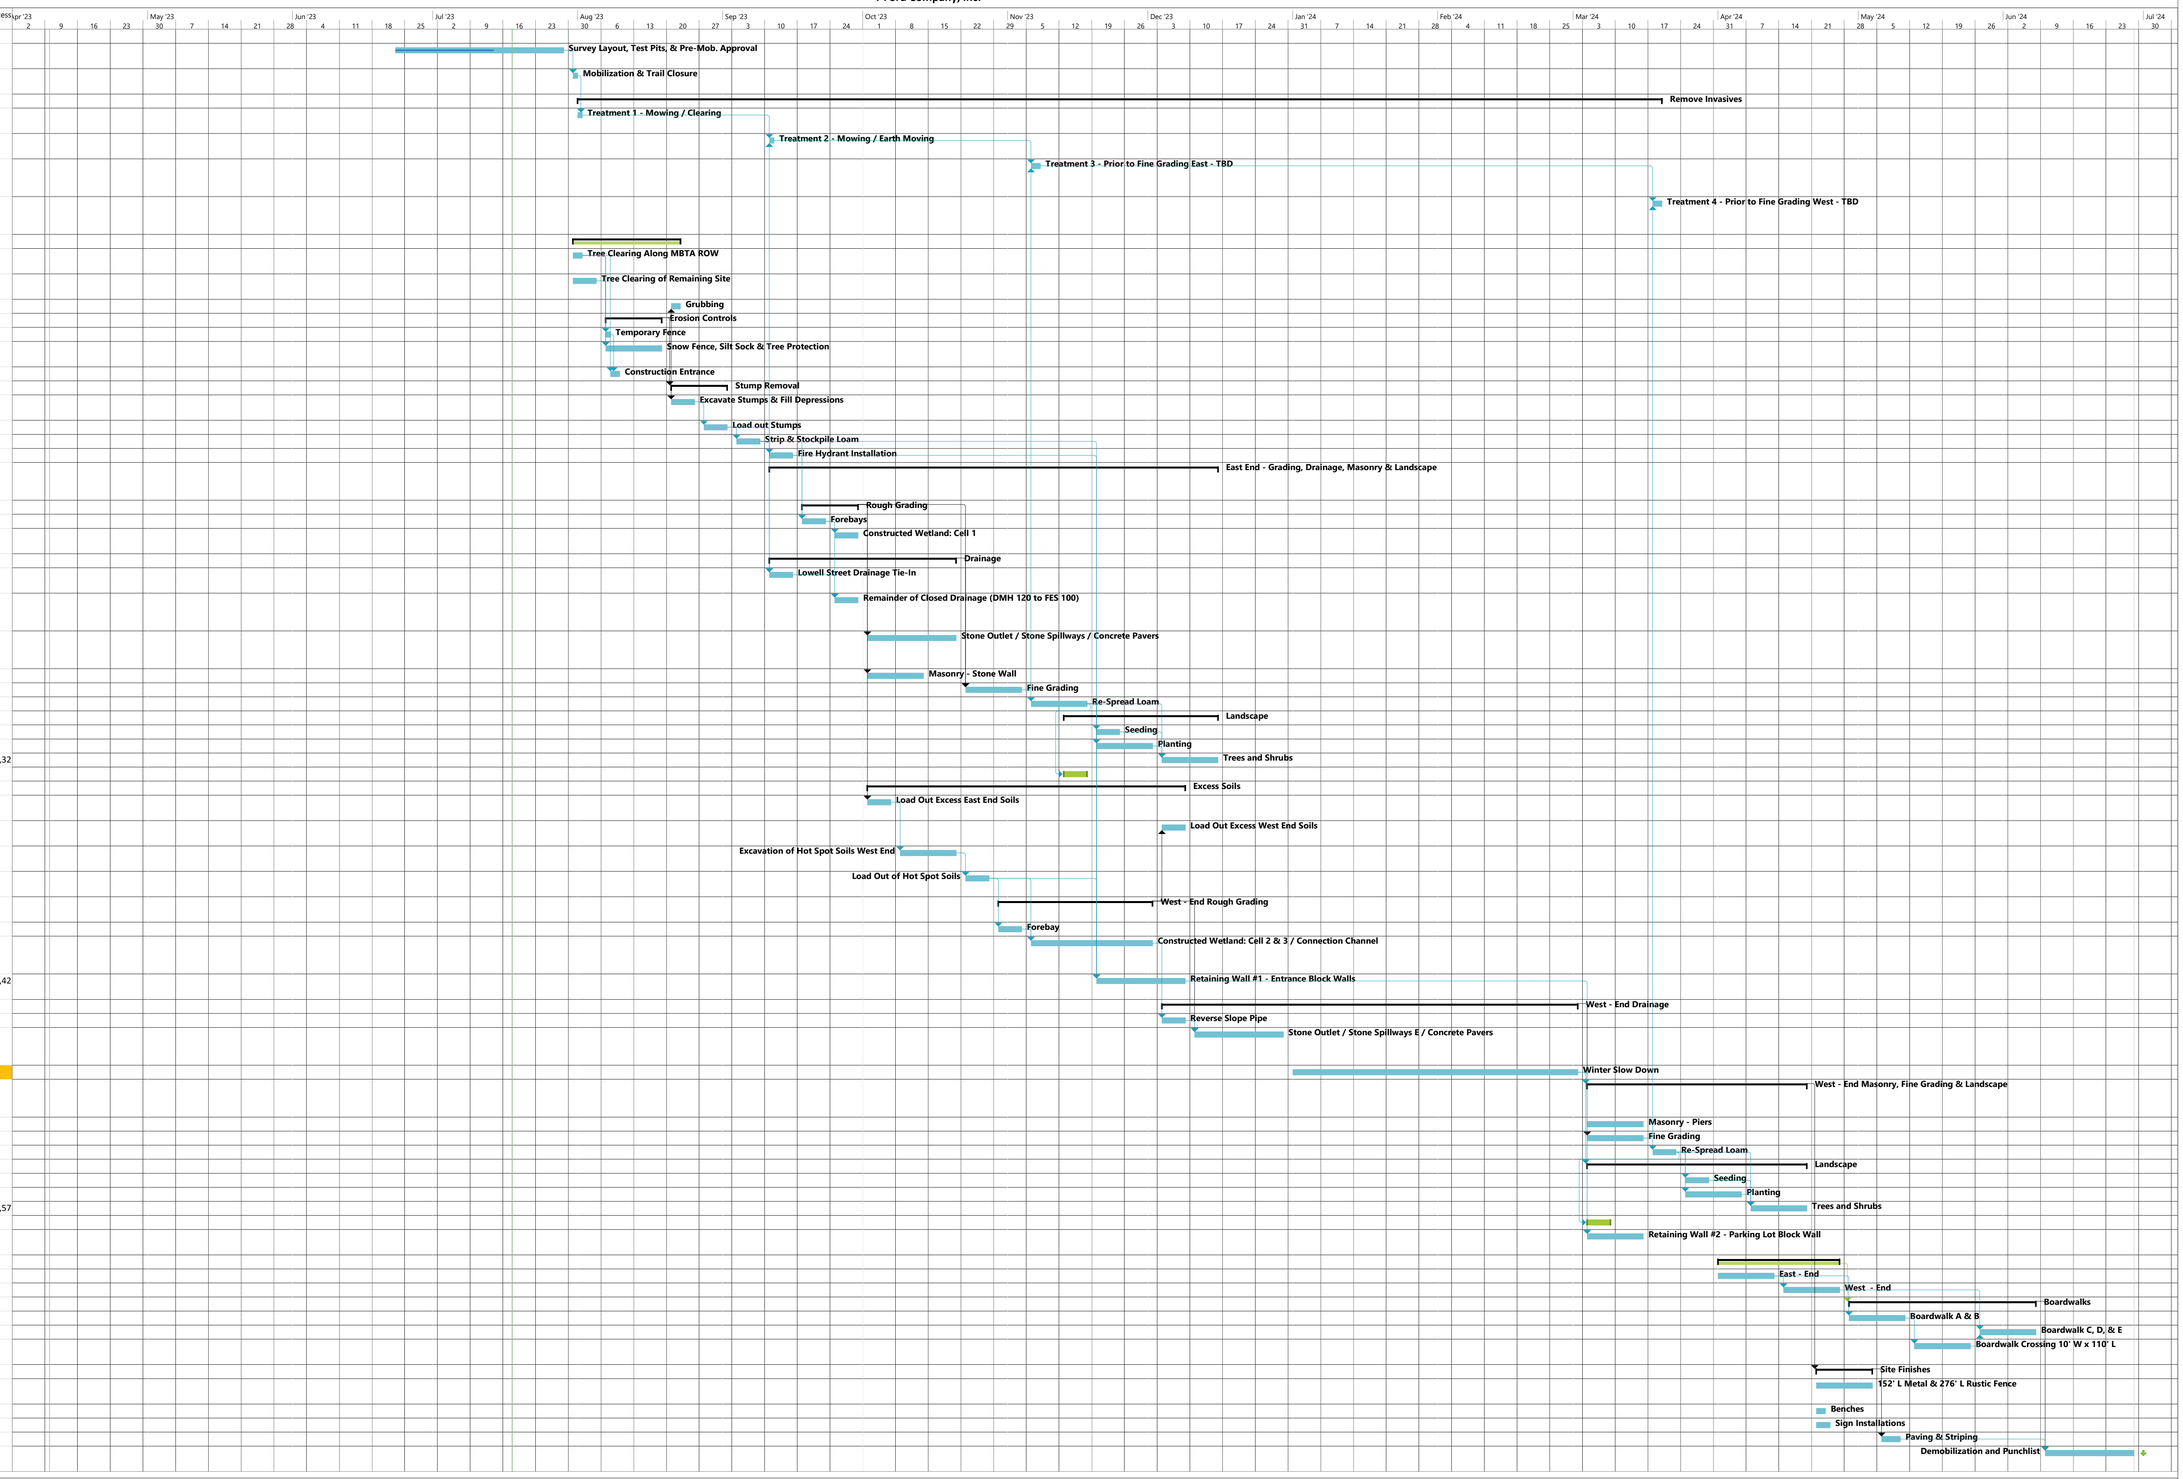

Project: Reading Baseline Sched
Date: Tue 7/18/23

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress
